Delivery 1 - Load 1 of 1 - Artic 13.6 m

12 pallets in 5 of 5 floor positions | 272 forms | tallest column 2522 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

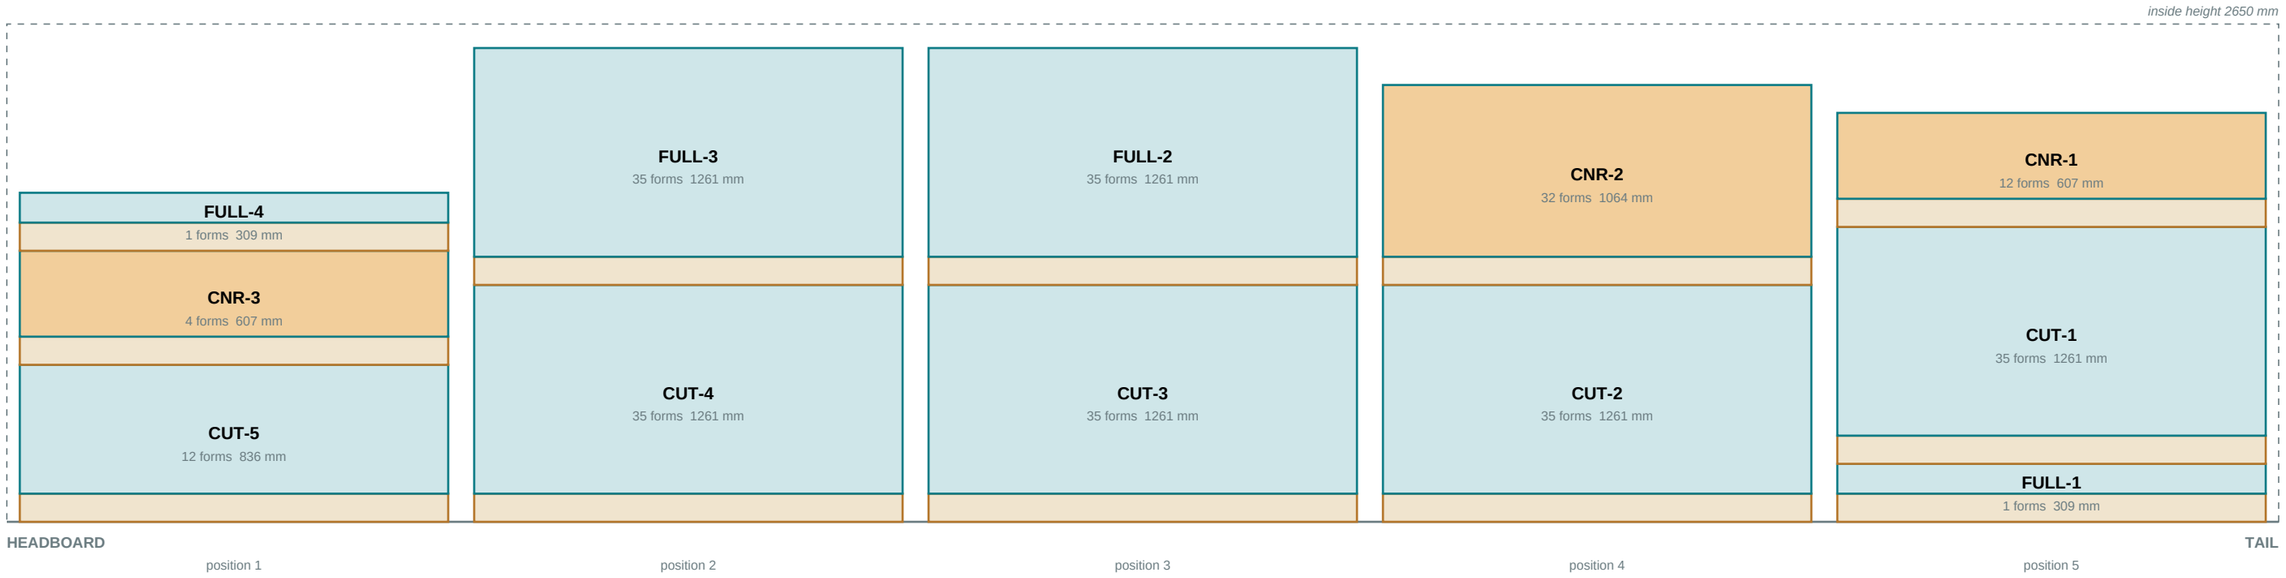

Unload order - 11 of 11 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 10in Std corners 12 forms courses P courses 1-3
2. CUT-1 10in Std straights 35 forms courses P courses 1-3
3. FULL-1 10in Std straights 1 forms courses P course 3
4. CNR-2 10in Std corners 32 forms courses B courses 1-8
5. CUT-2 10in Std straights 35 forms courses B courses 1-8
6. FULL-2 10in Std straights 35 forms courses B courses 2-5
7. CUT-3 10in Std straights 35 forms courses B courses 3-8
8. FULL-3 10in Std straights 35 forms courses B courses 5-8
9. CUT-4 10in Std straights 35 forms courses B courses 6-8
10. FULL-4 10in Std straights 1 forms courses B course 8
11. CNR-3 6in XR35 corners 4 forms courses FB courses 1-2
12. CUT-5 6in XR35 straights 12 forms courses FB courses 1-2

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-084 Keith Burrell - Plot 1 Rivendell Park…	FORMS	272
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	12	TALLEST	2522 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

8 pallets in 4 of 5 floor positions | 177 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

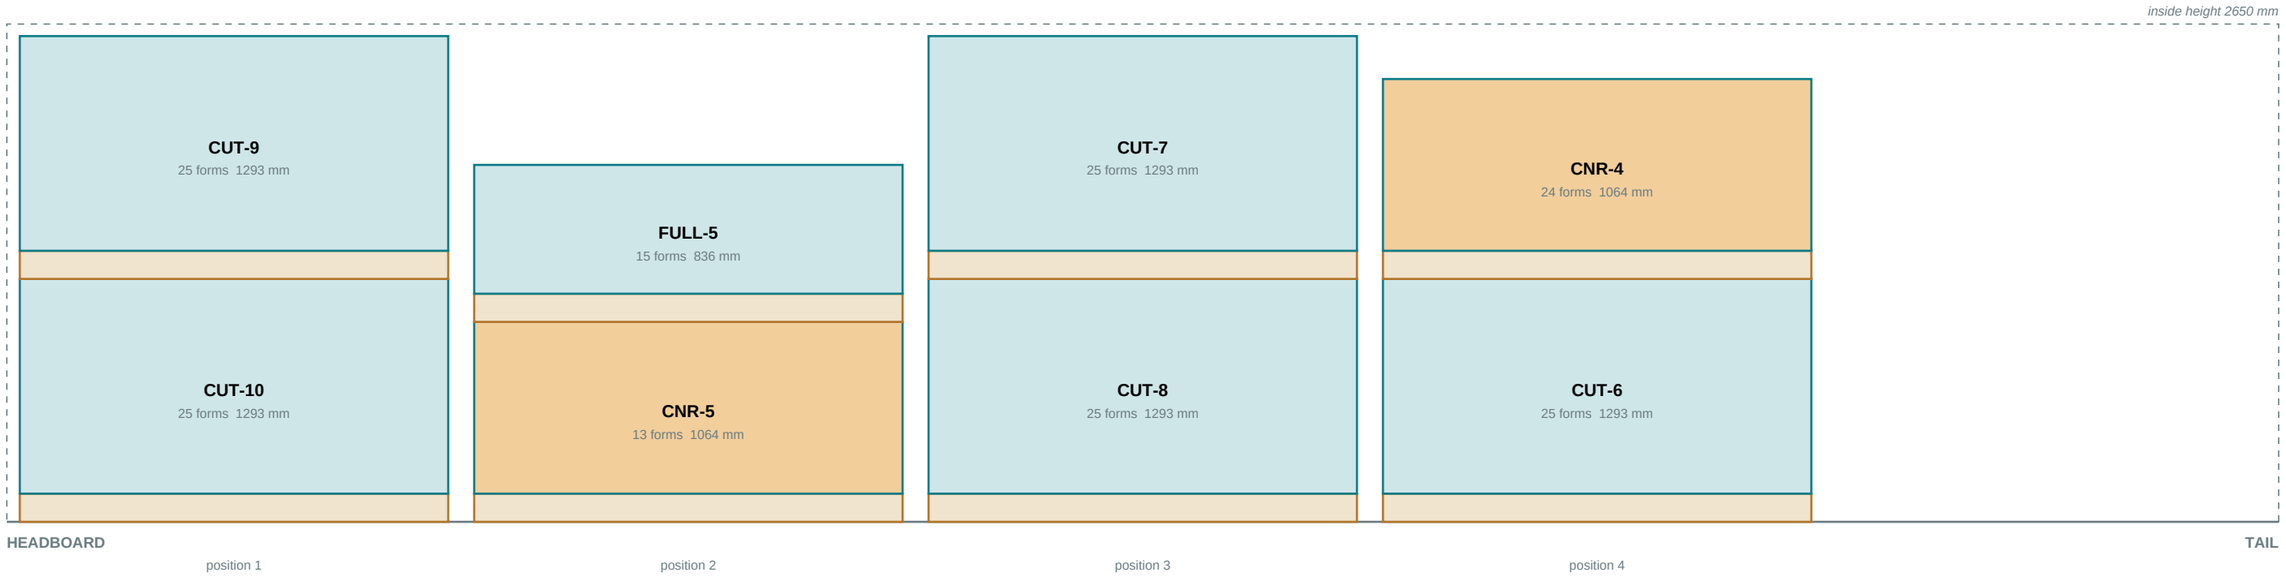

Unload order - 7 of 7 pallets come off out of build order, the price of stacking tallest forward

1. CNR-4 6in XR35 corners 24 forms courses L1 courses 1-5
2. CUT-6 6in XR35 straights 25 forms courses L1 courses 1-11
3. CUT-7 6in XR35 straights 25 forms courses L1 courses 2, 3, 4, 5, 6, 7, 8, 9, 10, 11
4. CUT-8 6in XR35 straights 25 forms courses L1 courses 3, 4, 5, 6, 7, 8, 9, 10, 13
5. FULL-5 6in XR35 straights 15 forms courses L1 courses 5-10
6. CNR-5 6in XR35 corners 13 forms courses L1 courses 5-11
7. CUT-9 6in XR35 straights 25 forms courses L1 courses 5, 6, 7, 8, 9, 10, 11, 13
8. CUT-10 6in XR35 straights 25 forms courses L1 courses 9-12

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-084 Keith Burrell - Plot 1 Rivendell Park…	FORMS	177
VEHICLE	Artic 13.6 m	POSITIONS	4 of 5
PALLETS	8	TALLEST	2586 mm
